Activity ID	Activity Name	RD	Start	Finish
I-10 Bayway Schedule		510	18-Sep-23 A	28-Oct-30
PROJECT ADMINISTRATION		487	23-May-24	28-Oct-30
SUMMARY		487	23-May-24	28-Oct-30
D1050	NTE Preconstruction Agreement	0		23-May-24
D9870	Conceptual Design Complete	0		02-Jul-24
D2890	USACE Issue - Joint Permit	0		15-Nov-24
D2940	ADEM Issue - Section 402 NPDES Permit	0		15-Nov-24
D2620	USCG Issue - USCG Bridge Permit (Tensaw, Apalachee, Blakeley River)	0		27-Nov-24
D5650	Final GMP - Guaranteed Maximum Price	0		27-Nov-24
A40840	Start of Construction	0	03-Feb-25*	
A58100	Finish of Construction	0		28-Oct-30
PERMITS		62	18-Sep-23 A	27-Nov-24
ENVIRONMENTAL/PERMITS		62	18-Sep-23 A	27-Nov-24
Government Approvals		62	18-Sep-23 A	27-Nov-24
401/404/10/WQC/CZM/408 Joint Permit (USACE)		60	18-Sep-23 A	15-Nov-24
Interagency Meetings		0	15-Nov-23 A	27-Mar-24
Section 9 Bridge Permit (USCG)		62	15-Nov-23 A	27-Nov-24
Nationwide Bridge Permit (NWP) 6 (Borings)		6	17-Nov-23 A	18-Mar-24
Section 402 NPDES Construction General Permit		15	24-May-24	11-Sep-24
NEPA Reevaluation		10	15-Mar-24	24-May-24
Federal Aviation Administration		3	24-May-24	17-Jun-24
PROCUREMENT		79	11-May-24	09-Jun-25
Gantry Cranes		79	11-May-24	09-Jun-25
CONSTRUCTION		434	03-Feb-25	28-Oct-30
US 98/90 OVERPASS		57	03-Feb-25	26-May-26
US 98/90 - Stage 1		19	03-Feb-25	10-Jul-25
US 98/90 - Stage 2		11	11-Jul-25	09-Oct-25
US 98/90 - Stage 3		8	10-Oct-25	15-Dec-25
US 98/90 - Stage 4		11	16-Dec-25	19-Mar-26
US 98/90 - Stage 5		8	20-Mar-26	26-May-26
MID BAY EASTBOUND (MBE)		419	03-Feb-25	17-Aug-30
BRIDGE		419	03-Feb-25	17-Aug-30
MIDBAY / (Sta. 562+61 to 724+75)		389	03-Feb-25	27-Mar-30
MID BAY RAMPS B & D		304	11-Aug-26	17-Aug-30
EAST MIDBAY / (Sta, 724+75 to 803+50)		99	14-Oct-26	19-Jan-29
TANGENT / (Sta. 803+50 to Sta.892+25)		15	04-Jan-29	04-May-29
MID BAY WESTBOUND (MBW)		419	03-Feb-25	17-Aug-30
ENVIRONMENTAL		4	03-Feb-25	06-Mar-25
BRIDGE		412	07-Mar-25	17-Aug-30
HLA / (Sta. 569+17 to 583+50)		192	07-Mar-25	10-Aug-29
WEST MIDBAY / Sta. 628+86 to Sta. 562+61)		120	07-Mar-25	10-Dec-27
TENSAW RIVER / (Sta. 614+70 to 628+86)		144	27-Mar-25	24-Jul-28
MIDBAY / (Sta. 562+61 to 724+75)		376	24-Apr-25	11-Apr-30
WEST TIE-IN / (Sta. 583+50 to 614+70)		132	23-Dec-25	11-Jan-29
MID BAY RAMPS A & C		304	11-Aug-26	17-Aug-30
EASTERN SHORE (ES)		434	03-Feb-25	28-Oct-30
ROADWAY/CIVIL/MOT		1	03-Feb-25	10-Feb-25
Eastern Shore - MOT		1	03-Feb-25	10-Feb-25
BRIDGE		432	11-Feb-25	28-Oct-30
EASTERN SHORE - WIDENING / (Sta. 917+25 to Sta.945+88)		432	11-Feb-25	28-Oct-30
EASTERN SHORE / (Sta. 892+25 to Sta.917+25)		130	30-Mar-26	27-Mar-29
TANGENT / (Sta. 803+50 to Sta.892+25)		97	11-Dec-26	12-Mar-29
EASTERN SHORE RAMP B		32	10-Feb-28	01-Nov-28
EASTERN SHORE RAMP A		32	02-Nov-28	01-Aug-29

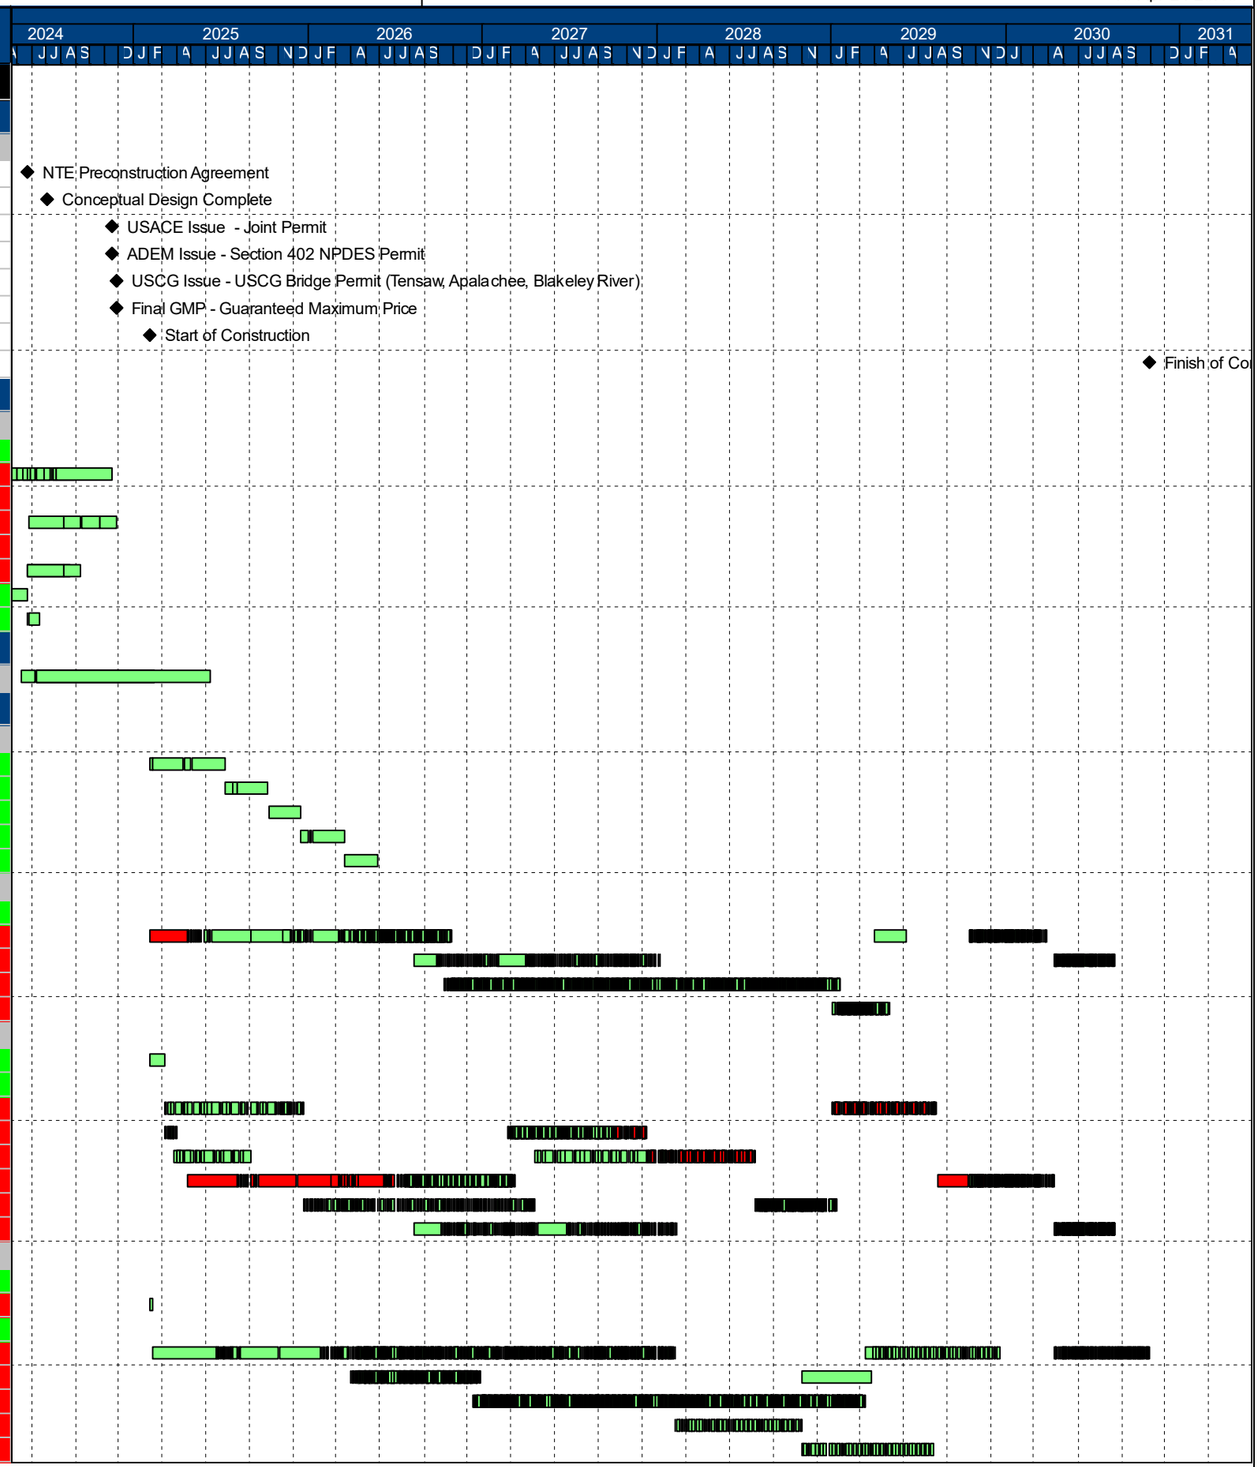

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
